Construction Clients Group Meeting 2020



Mieszko Iwaskow May 6th 2020



Coronavirus lockdown: NZ to hit Alert Level 4 Wednesday night

NEWS NATIONAL

NZ Herald, Mon, 23 Mar 2020, 1:44PM













LEVEL 4 AUCKLAND TRANSPORT CRISIS MANGEMENT TEAM CONSTRUCTION WORKSTREAM ACTIVITIES

1.	Project sites being monitored to ensure safety and Environmental compliance
2.	Contact Tree, connections and H&S Plan set up across the projects for essential workers performing site visits
3.	No- site productive work ongoing and looking at opportunities to accelerate
4.	Virtual working, team connectivity and social initiatives
5.	Scenario planning being progressed on bounce back as part of the business continuity plans update
6.	Commercial responses in line with direction from the Commercial Workstream Steering Group
7.	Ongoing reporting and controls more frequent governance Sessions with the Project Management Boards and PCGs





COVID-19 CONSTRUCTION WORKSTREAM LEVELS IMPACT

-evel 4 - Eliminate		LEVEL 4	Moderate Impact on programme delay, industry sustainability cost and ability to complete commitments	Significant Impact on programme delay, industry sustainability cost and ability to complete commitments	Severe Impact on programme delay, industry sustainability cost and ability to complete commitments
s not contained Level 3 - Restrict Heightened risk that disease is not contained	MPACT	FLUCTUATING 2-4	Moderate Impact on programme delay, industry sustainability cost and ability to site productivity	Significant Impact on programme delay, industry sustainability cost and site productivity	Significant Impact on programme delay, industry sustainability cost and site productivity
Level 2 - Reduce Disease is contained, but risks of community transmission growing	-	LEVEL 2 DROPPING	Moderate Impact on programme delay and cost but opportunity to bounce back, moderate impact on industry	Ability to de-risk some programme delays, will be overall cost increase, moderate impact on industry, new construction work can commence	Ability to de-risk some programme delays, will be overall cost increase, moderate impact on industry, new construction work can commence
evel 1 – Prepare ^{Disease is} ontained			1-3 MONTHS	3-6 MONTHS	6 MONTHS +

TIME





KARANGAHAPE ROAD




Surfacing decals designed to promote safe social distancing, using a rainbow design to embrace KRoads vibrant culture!









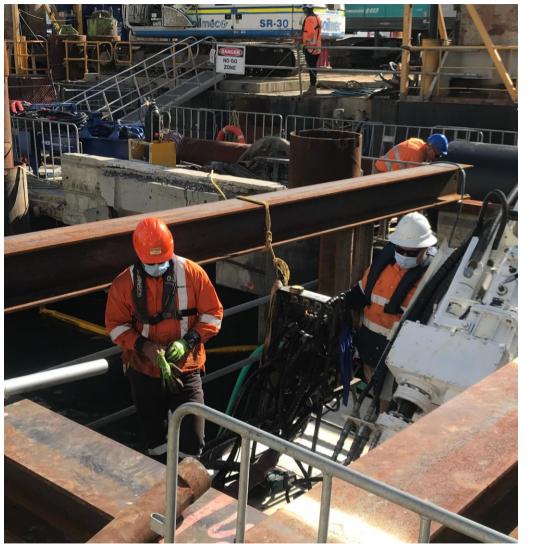

DOWNTOWN PROGRAMME

The Downtown Programme has moved smoothly into alert Level 3, restarting works across six of the seven DIDP projects. Around 190 staff have been divided into 28 "bubbles" where crews will remain to help reduce the likelihood of any exposure to the virus. Over the first few days the focus has been on educating teams on COVID -19 safety protocols and establishing new work routines in each bubble.





MARINE TEAM RETURN TO WORK...








Bubbles maintaining the appropriate social distancing.





DOWNTOWN SIGNAGE

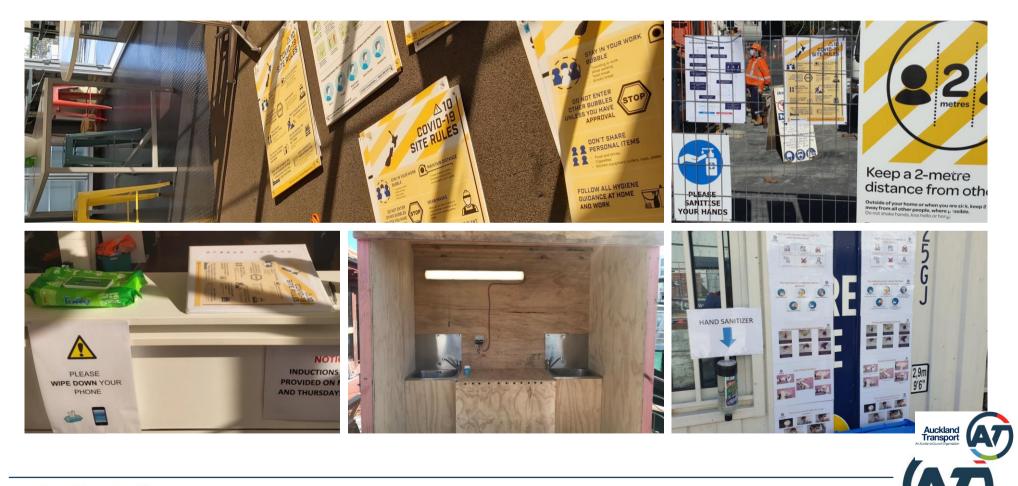



14

EASTERN BUSWAY 1 INITATIVES

15













"You have brains in your head. You have feet in your shoes. You can steer yourself any direction you choose."

Dr. Seuss

